

Newsletter 5 Bicycle parking Koningin Julianaplein Dd. 19 March 2018

In this newsletter, the municipality of The Hague and Mobilis provide you with information about the construction work for the underground bicycle parking on the Koningin Julianaplein. This newsletter is published every 2 months and is distributed in the immediate surrounding of Koningin Julianaplein and published on the website

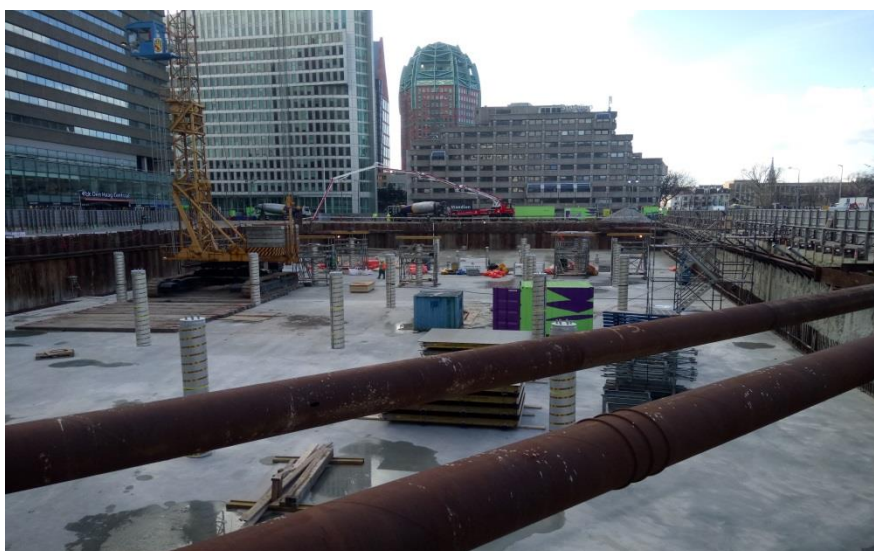


Figure 1. Building pit in the 8th February 2018

The building pit of the bicycle parking is excavated and concreted in two phases (see figure 2). Phase 1 is the workspace at the Bezuidenhoutseweg. The excavation of this phase started in October. Following the excavation, the walls, floors and decks of the bicycle parking are poured.

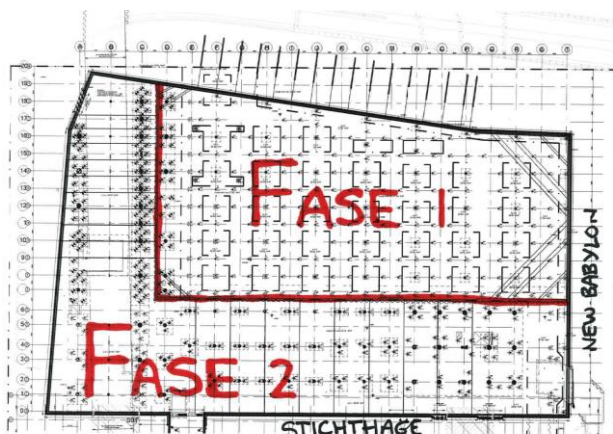


Figure 2. Phases

Work until today

Concreting of the floors of the bicycle parking

The first large concrete floor was poured on Friday, December 22, 2017. A beautiful December day with the nice weather. The concrete pouring of the floor was ready halfway through the day. On 25 January and 8 February (see figure 3) the rest of the floor was poured. Especially February the 8th was a cold day. By using stoves it has been possible to pour the concrete floor. Meanwhile, the entire floor of phase 1 has been poured.

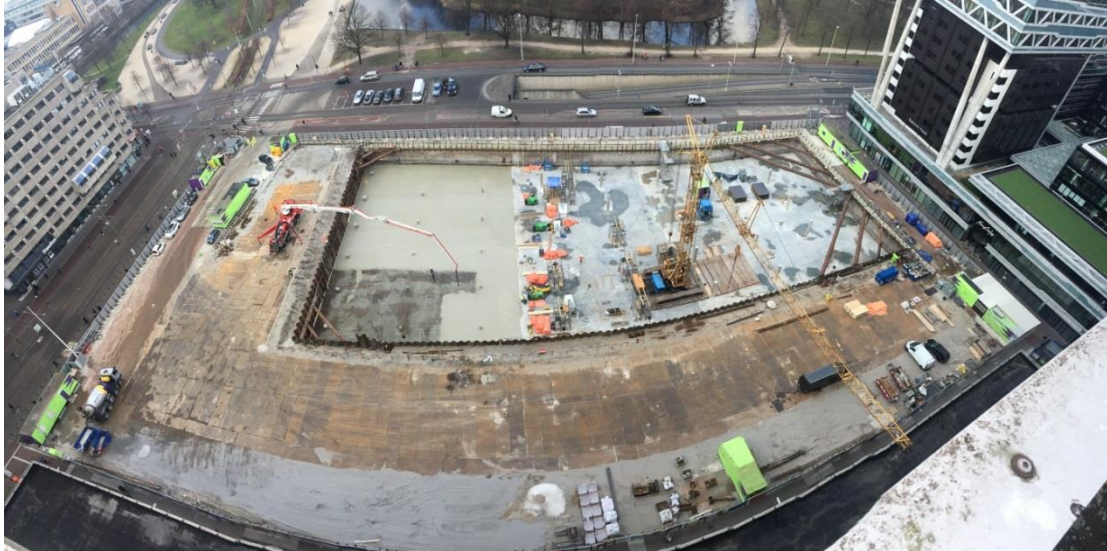


Figure 3. Concrete pouring of the floor

Concreting the walls of the bicycle storage

The walls are installed after the floors. For this, the support construction of the walls of building pit have been removed. The weather conditions were not ideal for pouring concrete. To protect the hardening process, freshly poured concrete is covered (see figure 4).

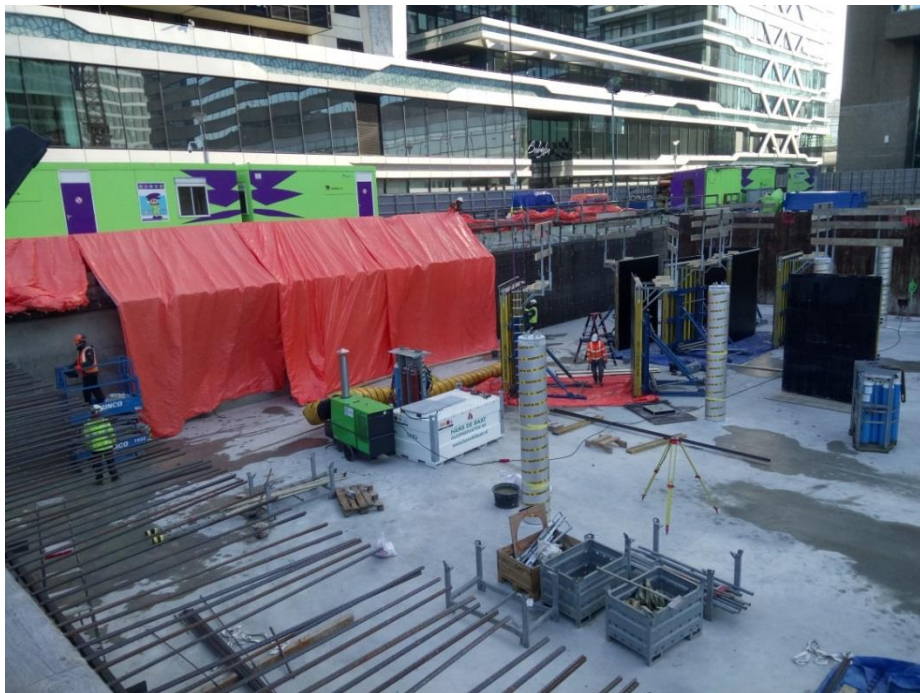


Figure 4. Pouring of the walls

Preview

Making the walls & deck

Currently, the concrete work of phase 1 is being completed. In small works the walls are made on the site of the Bezuidenhoutseweg. Then we will pour the deck and the pillars. The deck will be visible as a ceiling for the bicycle parking; the pillars are visible as columns.

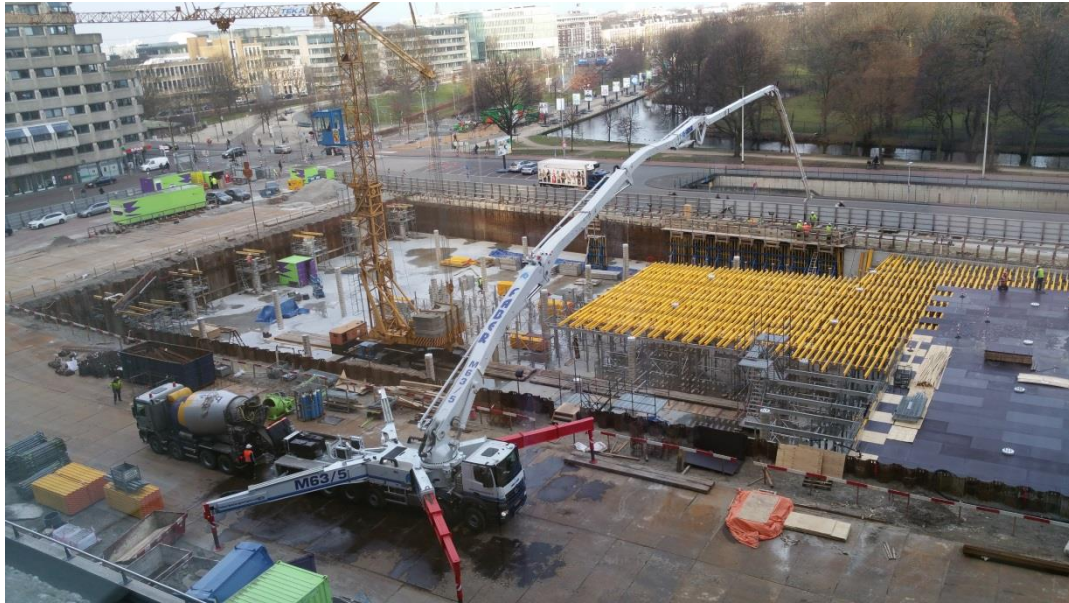


Figure 5. The formwork of the deck (made by: Rene Middel)

Excavating Phase 2

In the course of April we will start with the construction of phase 2. The building pit will be further excavated, the support structure will be placed and the floors, walls, pillars and deck will be poured.

Applying two additional entrances to Bezuidenhoutseweg side

In order to be able to work on phase 2, work is being done from the deck of phase 1. Two extra entrances are made to the building site on the Bezuidenhoutseweg side.

Taking down parts of the pillars at the site of Stichthage

The applied foundation piles and CSM wall along the façade of Stichthage form a supporting construction for the deck and the new buildings. In order to get to the correct height from the deck, the top side off the wall and the pillars will be taking down. We are currently investigating how these activities can best be carried out in order to limit the inconvenience as much as possible.

Website

The website www.kj-plein.nl always contains the most recent information about the project. Since 1 September 2017 there are 2 webcams on the roof of the Stichthage building. This allows the construction via the website 24/7 to follow.

Information about the new buildings can be found on www.kjdenhaag.nl

Walk-in consultation hour

For information and questions about the construction work, you are welcome every Monday between 8.30 and 9.30 am at the walk-in office on the 9th floor of the Stichthage building. Eva Zonneveld, the environment manager of Mobilis, will be present here.

Contact

If you have any further questions about this letter, please feel free to contact us. This can be done via the contact form on our website www.kj-plein.nl. You can also reach us via the address info@kj-plein.nl. And of course you are more than welcome at the walk-in consultation hour.

If you see something suspicious during the works or want to report a calamity, you can reach us 24/7 on our emergency number: 06-21504617.
